



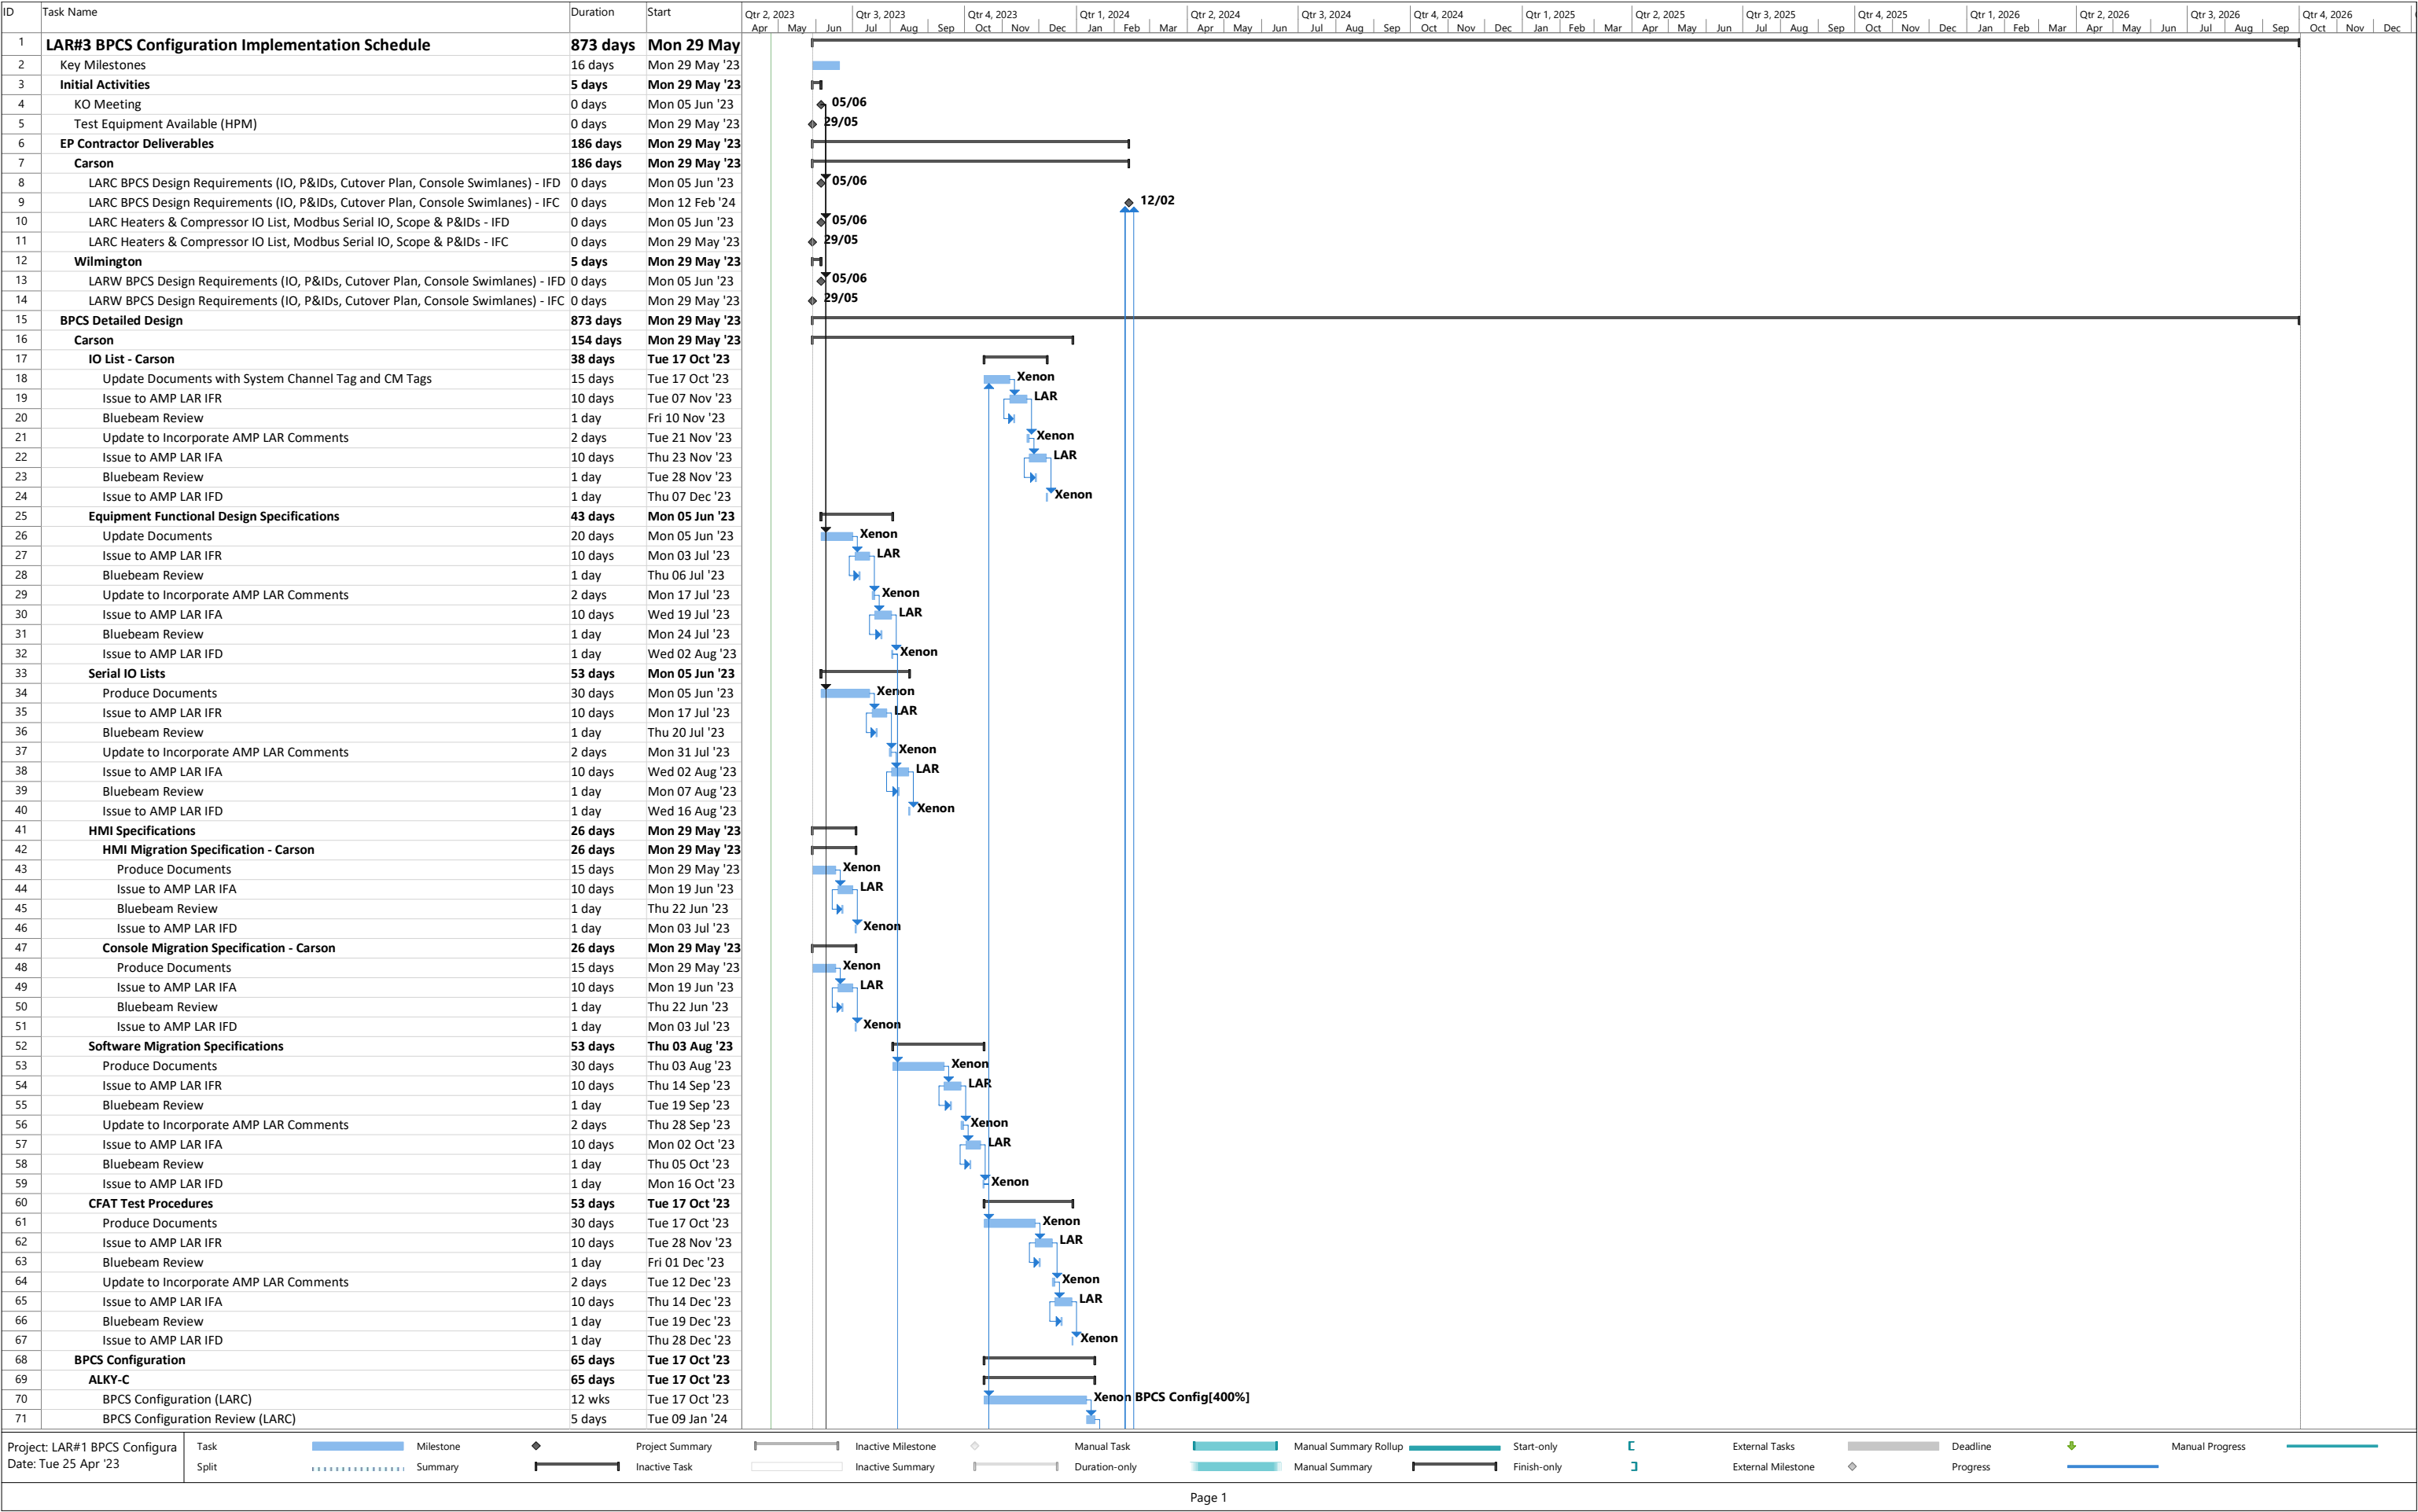

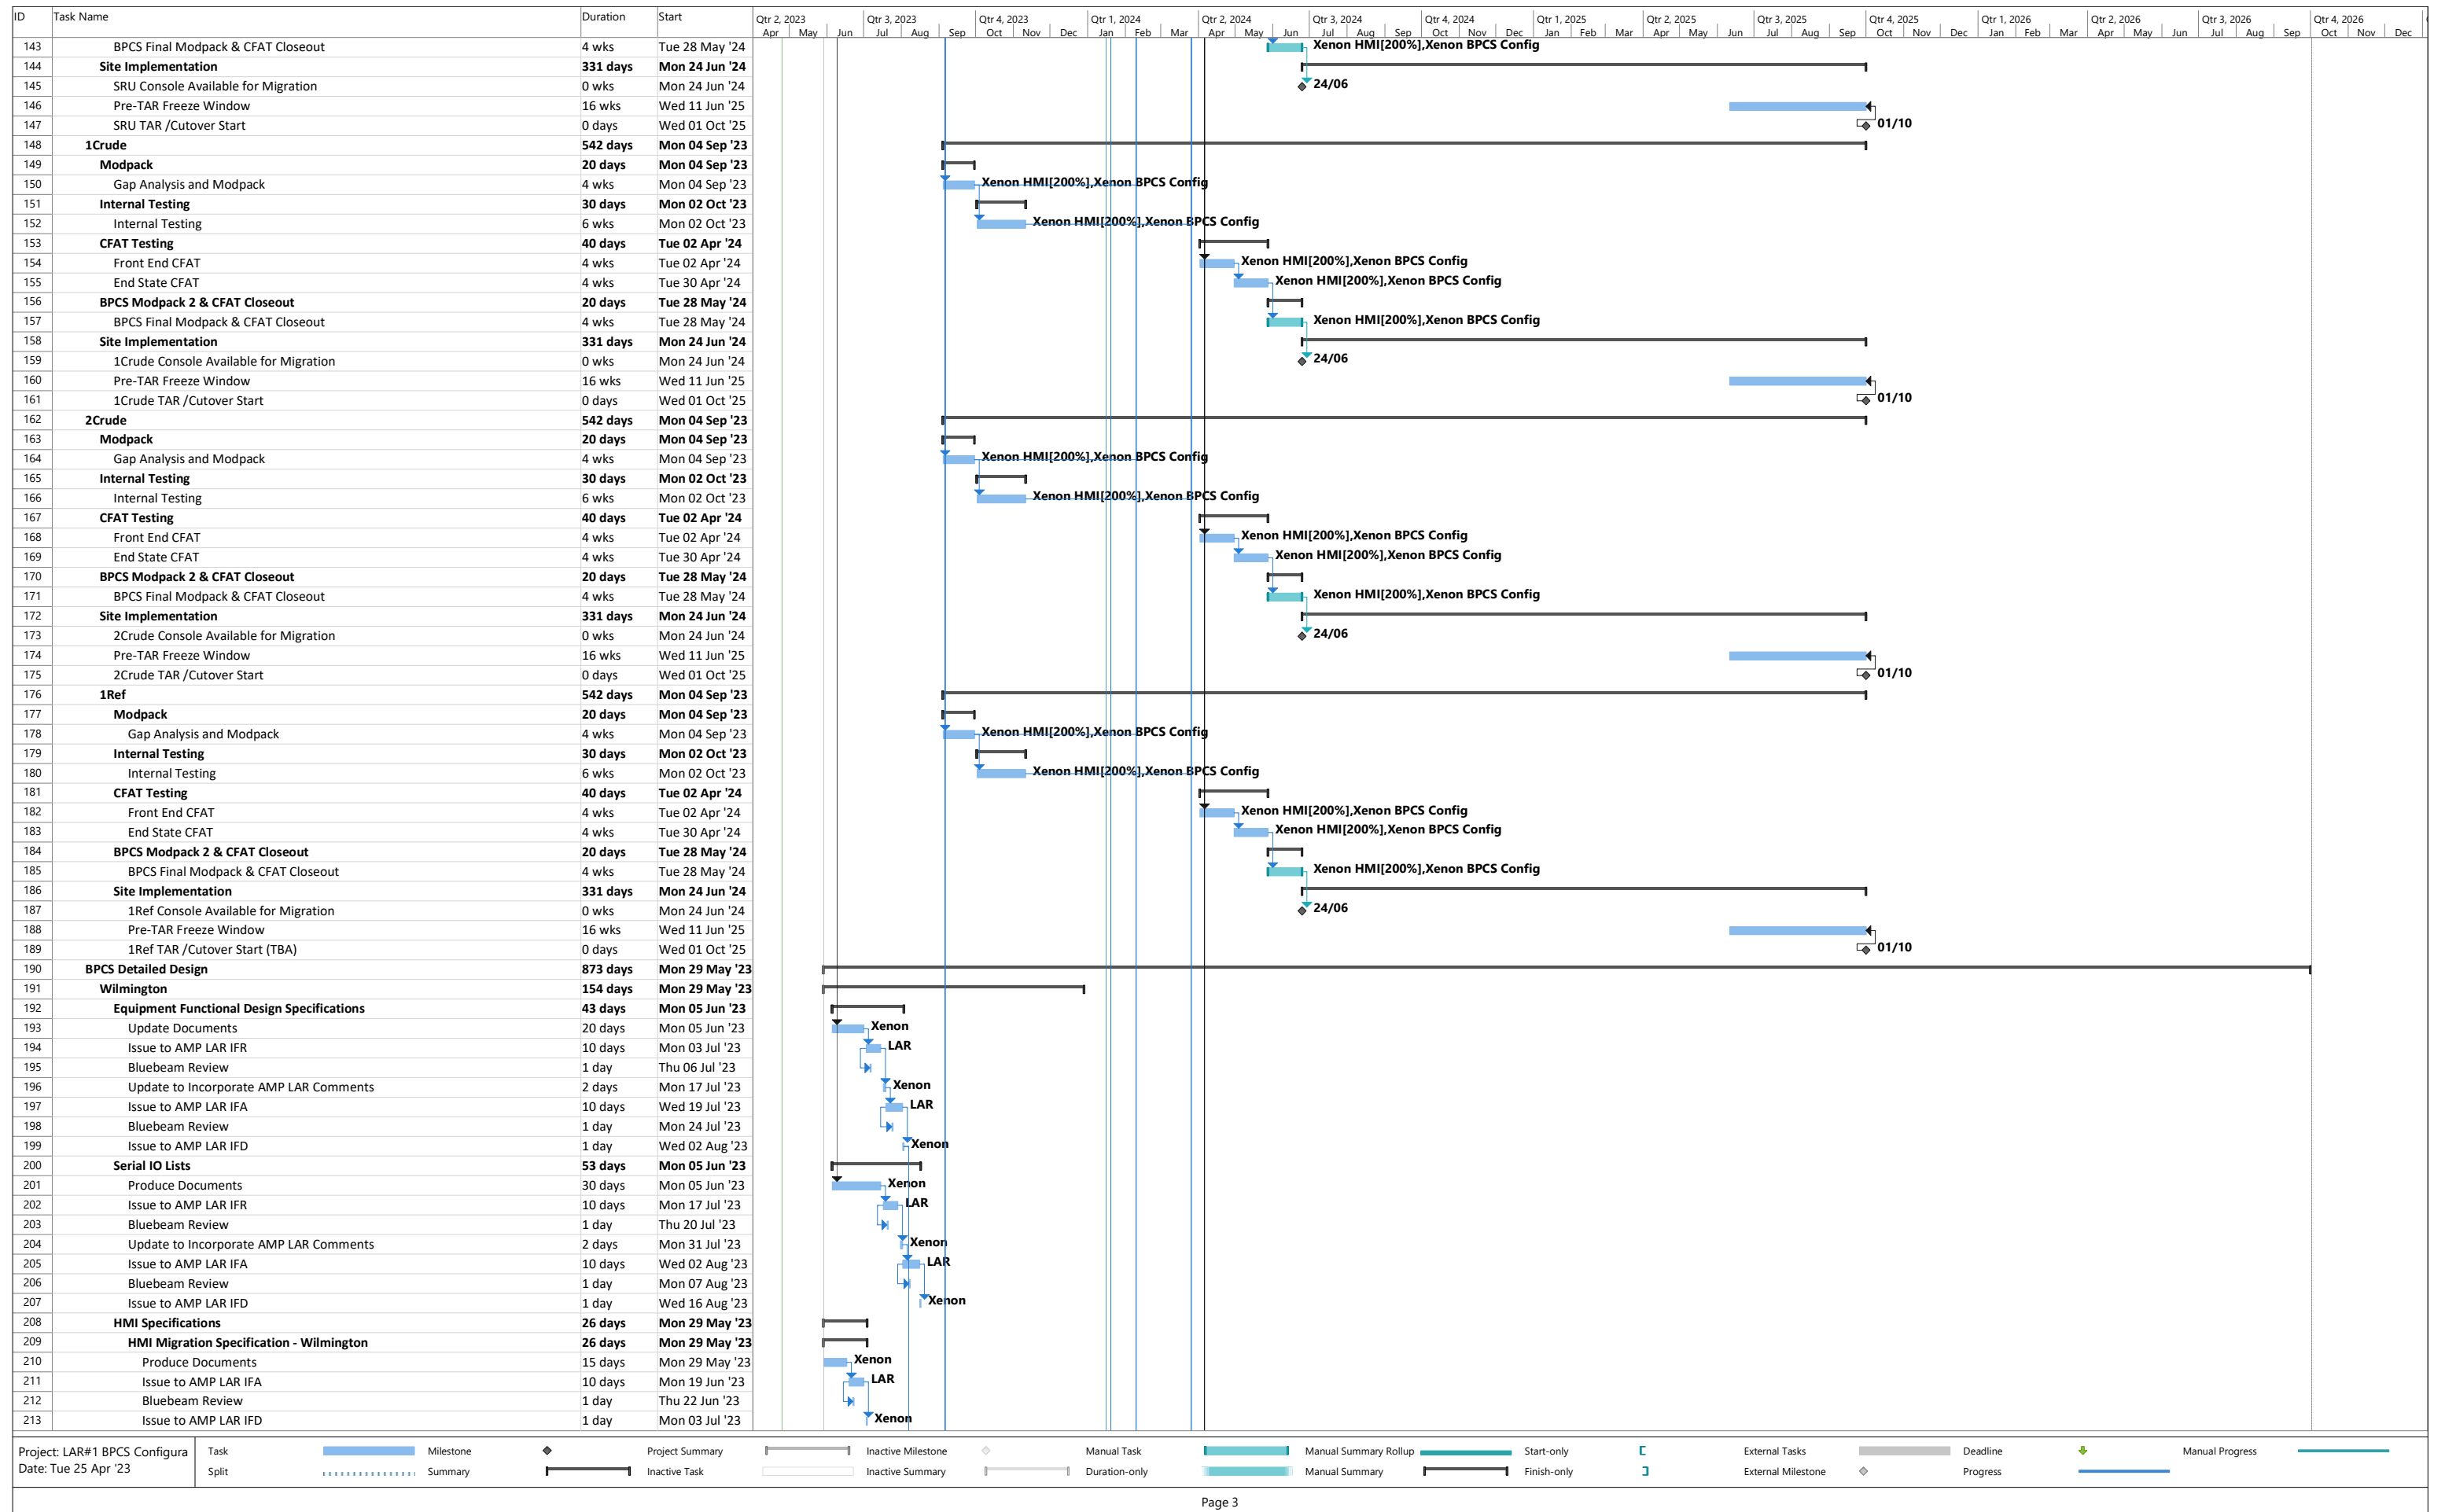

ID	Task Name	Duration	Start
214	Console Migration Specification - Wilmington	26 days	Mon 29 May '23
215	Produce Documents	15 days	Mon 29 May '23
216	Issue to AMP LAR IFA	10 days	Mon 19 Jun '23
217	Bluebeam Review	1 day	Thu 22 Jun '23
218	Issue to AMP LAR IFD	1 day	Mon 03 Jul '23
219	Software Migration Specifications	53 days	Thu 03 Aug '23
220	Produce Documents	30 days	Thu 03 Aug '23
221	Issue to AMP LAR IFR	10 days	Thu 14 Sep '23
222	Bluebeam Review	1 day	Tue 19 Sep '23
223	Update to Incorporate AMP LAR Comments	2 days	Thu 28 Sep '23
224	Issue to AMP LAR IFA	10 days	Mon 02 Oct '23
225	Bluebeam Review	1 day	Thu 05 Oct '23
226	Issue to AMP LAR IFD	1 day	Mon 16 Oct '23
227	CFAT Test Procedures	53 days	Tue 17 Oct '23
228	Produce Documents	30 days	Tue 17 Oct '23
229	Issue to AMP LAR IFR	10 days	Tue 28 Nov '23
230	Bluebeam Review	1 day	Fri 01 Dec '23
231	Update to Incorporate AMP LAR Comments	2 days	Tue 12 Dec '23
232	Issue to AMP LAR IFA	10 days	Thu 14 Dec '23
233	Bluebeam Review	1 day	Tue 19 Dec '23
234	Issue to AMP LAR IFD	1 day	Thu 28 Dec '23
235	BPCS Configuration	65 days	Tue 17 Oct '23
236	W-HCU	65 days	Tue 17 Oct '23
237	BPCS Configuration (LARW)	12 wks	Tue 17 Oct '23
238	BPCS Configuration Review (LARW)	5 days	Tue 09 Jan '24
239	HGU-2	65 days	Tue 17 Oct '23
240	BPCS Configuration (LARC)	12 wks	Tue 17 Oct '23
241	BPCS Configuration Review (LARC)	5 days	Tue 09 Jan '24
242	HMI Configuration	118 days	Mon 29 May '23
243	W-HCU	70 days	Thu 03 Aug '23
244	Develop HMI Screens - Wilmington	14 wks	Thu 03 Aug '23
245	HGU-2	70 days	Mon 29 May '23
246	Develop HMI Screens - Wilmington	14 wks	Mon 29 May '23
247	W-HCU	803 days	Mon 04 Sep '23
248	Modpack	20 days	Mon 04 Sep '23
249	Gap Analysis and Modpack	4 wks	Mon 04 Sep '23
250	Internal Testing	30 days	Mon 02 Oct '23
251	Internal Testing	6 wks	Mon 02 Oct '23
252	CFAT Testing	40 days	Tue 02 Apr '24
253	Front End CFAT	4 wks	Tue 02 Apr '24
254	End State CFAT	4 wks	Tue 30 Apr '24
255	BPCS Modpack 2 & CFAT Closeout	20 days	Tue 28 May '24
256	BPCS Final Modpack & CFAT Closeout	4 wks	Tue 28 May '24
257	Site Implementation	592 days	Mon 24 Jun '24
258	W-HCU Console Available for Migration	0 wks	Mon 24 Jun '24
259	Pre-TAR Freeze Window	16 wks	Thu 11 Jun '26
260	W-HCU TAR /Cutover Start	0 days	Thu 01 Oct '26
261	W-HGU-2	475 days	Mon 04 Sep '23
262	Modpack	20 days	Mon 04 Sep '23
263	Gap Analysis and Modpack	4 wks	Mon 04 Sep '23
264	Internal Testing	30 days	Mon 02 Oct '23
265	Internal Testing	6 wks	Mon 02 Oct '23
266	CFAT Testing	40 days	Tue 02 Apr '24
267	Front End CFAT	4 wks	Tue 02 Apr '24
268	End State CFAT	4 wks	Tue 30 Apr '24
269	BPCS Modpack 2 & CFAT Closeout	20 days	Tue 28 May '24
270	BPCS Final Modpack & CFAT Closeout	4 wks	Tue 28 May '24
271	Site Implementation	264 days	Mon 24 Jun '24
272	W-HGU-2 Console Available for Migration	0 wks	Mon 24 Jun '24
273	Pre-TAR Freeze Window	16 wks	Mon 10 Mar '25
274	W-HGU-2TAR /Cutover Start	0 days	Mon 30 Jun '25

Project: LAR#1 BPCS Configura
Date: Tue 25 Apr '23

Task Split

Milestone Summary

Project Summary Inactive Task

Inactive Milestone Inactive Summary

Manual Task Duration-only

Manual Summary Rollup Manual Summary

Start-only Finish-only

External Tasks External Milestone

Deadline Progress

Manual Progress

Page 4
